

Quarterly progress of various components of the project

Status for 1st Quarter 2018:

TOWER 1

- Foundations are 100% complete.
- Slab from 3rd basement to Ground Floor level are 100% complete.
- Upper Ground Floor Level Slab is in progress.

TOWER 2

- Foundations are 100% complete.
- Slab at 2nd & 1st basement floor level is in Progress.



TOWER 3

- Foundations are 100% complete.
- 3rd & 2nd Basement Slab are in Progress.

Quarterly schedule of construction of infrastructure facilities.

Retaining Wall Construction is in Progress.

Quarterly schedule of construction of the apartments.

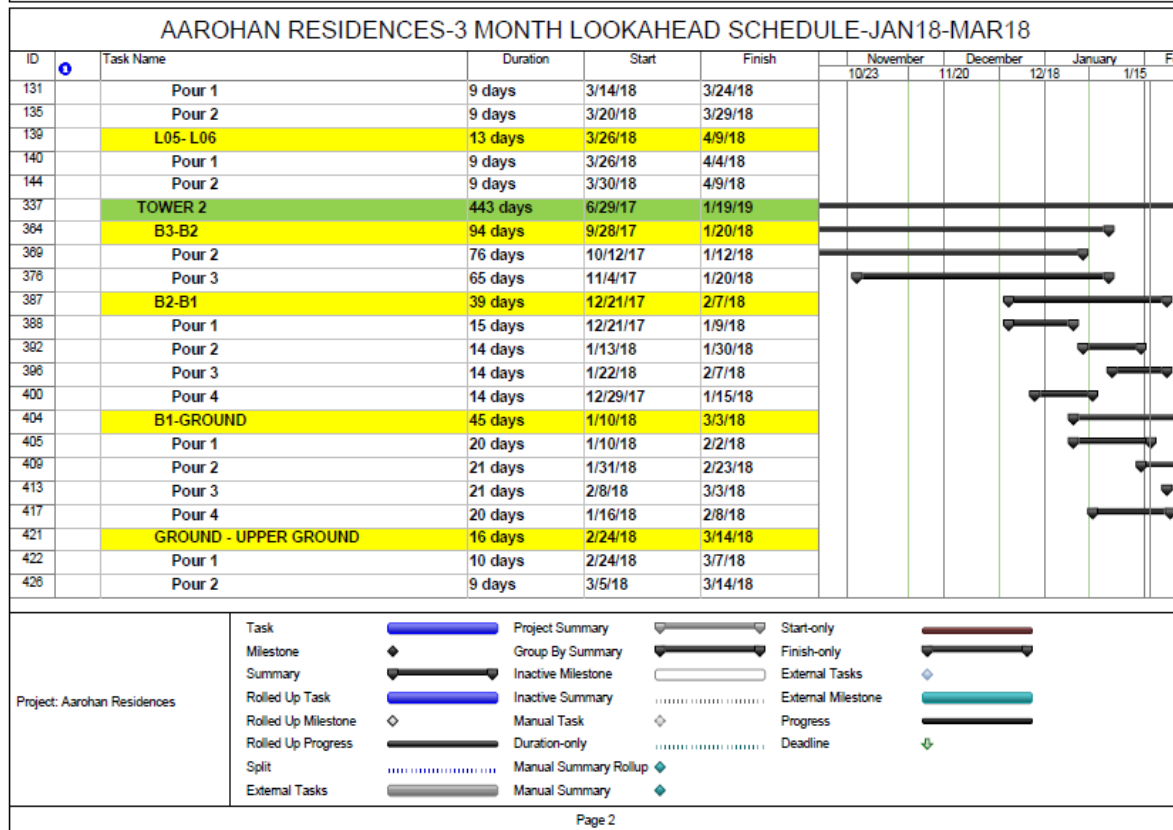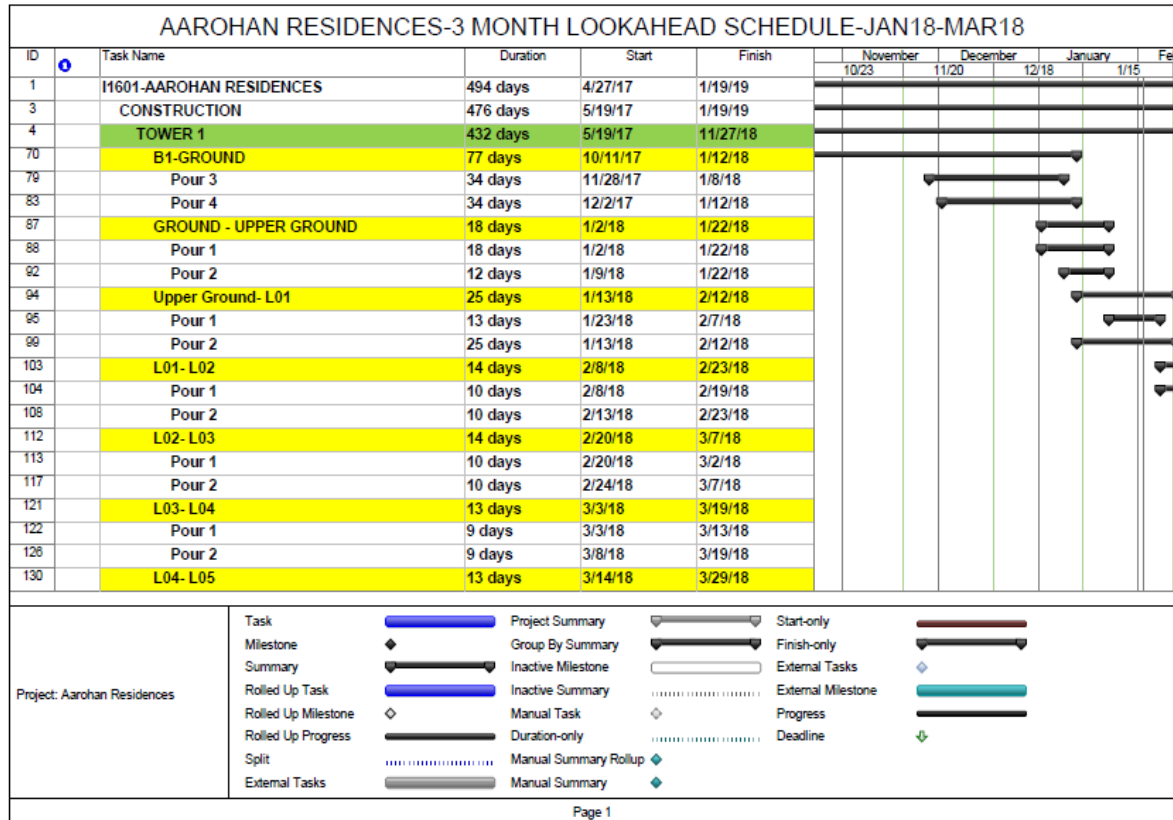

AAROHAN RESIDENCES-3 MONTH LOOKAHEAD SCHEDULE-JAN18-MAR18

ID	Task Name	Duration	Start	Finish	November	December	January	February
					10/23	11/20	12/18	1/15
430	Upper Ground- L01	15 days	3/8/18	3/26/18				
431	Pour 1	9 days	3/8/18	3/19/18				
435	Pour 2	9 days	3/15/18	3/26/18				
439	L01- L02	15 days	3/20/18	4/5/18				
440	Pour 1	9 days	3/20/18	3/29/18				
444	Pour 2	9 days	3/27/18	4/5/18				
448	L02- L03	14 days	3/30/18	4/14/18				
449	Pour 1	8 days	3/30/18	4/7/18				
700	TOWER 3	411 days	7/25/17	1/3/19				
727	B3-B2	67 days	11/16/17	2/5/18				
728	Pour 1	48 days	11/16/17	1/12/18				
732	Pour 2	52 days	11/23/17	1/24/18				
739	Pour 3	52 days	12/4/17	2/5/18				
746	Pour 4	20 days	1/5/18	1/29/18				
750	B2-B1	33 days	1/13/18	2/21/18				
751	Pour 1	16 days	1/13/18	2/1/18				
755	Pour 2	15 days	1/25/18	2/12/18				
759	Pour 3	14 days	2/6/18	2/21/18				
763	Pour 4	13 days	1/31/18	2/14/18				
767	B1 - GROUND	36 days	2/2/18	3/15/18				
768	Pour 1	21 days	2/2/18	2/26/18				
772	Pour 2	20 days	2/13/18	3/7/18				

Project: Aarohan Residences	Task		Project Summary		Start-only	
	Milestone		Group By Summary		Finish-only	
	Summary		Inactive Milestone		External Tasks	
	Rolled Up Task		Inactive Summary		External Milestone	
	Rolled Up Milestone		Manual Task		Progress	
	Rolled Up Progress		Duration-only		Deadline	
	Split		Manual Summary Rollup			
	External Tasks		Manual Summary			

Page 3

AAROHAN RESIDENCES-3 MONTH LOOKAHEAD SCHEDULE-JAN18-MAR18

ID	Task Name	Duration	Start	Finish	November	December	January	February
					10/23	11/20	12/18	1/15
776	Pour 3	19 days	2/22/18	3/15/18				
780	Pour 4	19 days	2/15/18	3/8/18				
784	GROUND - UPPER GROUND	17 days	3/8/18	3/28/18				
785	Pour 1	13 days	3/8/18	3/23/18				
789	Pour 2	10 days	3/16/18	3/28/18				
793	Upper Ground- L01	14 days	3/24/18	4/9/18				
794	Pour 1	10 days	3/24/18	4/4/18				
798	Pour 2	10 days	3/29/18	4/9/18				
1027	RETAINING WALL	230 days	5/19/17	3/9/18				
1040	PART D - 50M (DG AREA)	25 days	12/28/17	1/27/18				
1044	PART E - 50M	22 days	2/13/18	3/9/18				
1048	NON TOWER	62 days	1/6/18	3/21/18				
1049	Pour 1	62 days	1/6/18	3/21/18				
1050	POUR 1	48 days	1/6/18	3/3/18				
1051	Foundation	28 days	1/6/18	2/8/18				
1057	B3-B2	25 days	2/3/18	3/3/18				
1058	Columns	15 days	2/3/18	2/20/18				
1059	Slab Shuttering & Reinforcement	14 days	2/14/18	3/1/18				
1060	Concrete	2 days	3/2/18	3/3/18				
1061	POUR 2	48 days	1/23/18	3/21/18				
1062	Foundation	28 days	1/23/18	2/24/18				
1068	B3-B2	25 days	2/20/18	3/21/18				

Project: Aarohan Residences	Task		Project Summary		Start-only	
	Milestone		Group By Summary		Finish-only	
	Summary		Inactive Milestone		External Tasks	
	Rolled Up Task		Inactive Summary		External Milestone	
	Rolled Up Milestone		Manual Task		Progress	
	Rolled Up Progress		Duration-only		Deadline	
	Split		Manual Summary Rollup			
	External Tasks		Manual Summary			

Page 4
